CONFIDENTIAL MARCH 2026

Sportsbook Programme

World Cup MVP Delivery Plan

16	4	8
WORK PACKAGES	DELIVERABLES	DOMAIN TEAMS

Apr 1
Soft Launch

May 1
Go-Live

Mid-June
World Cup Kick-Off

v1.55: Straights only • v1.6: + Parlay + SGP + Mega • Soccer • Pre-match • USD • en-US • 4 brands

Summary of Updates — 31 Mar 2026

Key progress reflected from Jira SBK-669 Initiative and contributing Epics.

SIGNIFICANT PROGRESS

- **Overall Program:** Jumped from 23% to **59% complete**.
- **Simple Parlay (SBK-2199):** Now **85% complete** (up from 32%).
- **Market Parser (SBK-1897):** Reached **91% complete** (up from 45%).
- **Settlement (SBK-2200):** Progressed to **67% complete**.

KEY MILESTONE UPDATES

- **Central Offer (SBK-3006):** Moved to **59% complete**, unblocking downstream dependencies.
- **Straight Bet (SBK-1951):** Frontend reached **59% complete**.
- **Audit Trail (SA-28):** Status moved to **In Delivery** as architecture implementation begins.
- **Feed Health (SBK-3094):** Initial tracking established at **40% complete**.

Data Integrity Note:

All metrics on Slide 17 (Epic Progress) have been synchronized with the live ticket status counts in Jira. Total ticket count increased to 139 as team-specific tasks were refined. The "Today" marker on the timeline has been moved to March 31.

4 Deliverables — Each a Demoable Increment

The programme is structured so each deliverable adds visible business value across all teams in parallel.

1. CENTRAL OFFERING FOUNDATION

OFFER

Punter opens the sportsbook and browses World Cup fixtures with live odds

6 WPs • FEEDS, OFFER, FRONTEND, BETTING, DATA

2. BETSLIP CORE & PLACEMENT

BETTING

Punter builds a bet, places it, gets validated. Operator controls limits and kill switch

11 WPs • FRONTEND, BETTING, OFFER, DATA

3. MY BETS & REAL DATA

SETTLEMENT

Bets settle from real results. Real money moves. Punter sees bet history live

10 WPs • BETTING, DATA, FRONTEND, FEEDS, OFFER

4. OPERATION CONTROL & VISIBILITY

OPERATIONS

Traders manage the book via Kraken. Splunk dashboards show the full operational picture

14 WPs • BACKOFFICE, BETTING, DATA, SPLUNK

16 Work Packages

Each WP is a scoped, architecture-reviewed unit of work delivering a specific business capability.

#	WORK PACKAGE	WHAT IT DELIVERS	#	WORK PACKAGE	WHAT IT DELIVERS
1	Simple Parlay	Combine bets from different matches	9	Manual Resettlement	Traders correct grading errors and void bets
2	Soccer WC Hub	World Cup landing page with fixtures & markets	10	Audit Trail	Who changed what, when, why
3	Settlement	Auto-grade and settle bets from real results	11	RT Odds Display	Live odds updates + suspended market indicators
4	Book On/Off Switch	Emergency kill switch + punter blocking	12	My Bets	Punter checks active and settled bets
5	Bet Placement Controls	Stake limits, payout caps, odds validation	13	Bet History	Traders investigate punter betting activity
6	Central Offer Foundation	Own our offer data, not the feed provider's	14	SGP	Same-game parlay with correlated pricing
7	Bet Ticker	Live bet feed for traders	15	Mega Parlay	SGPs + straights across matches — premium bet
8	RT Liability	Real-time book exposure by market	16	Feed Health	Detect unhealthy feeds, protect from stale data

Work Package Status

LIVE FROM JIRA • 31 MAR 2026

1	12	3	2
COMPLETED	IN DELIVERY	READY FOR HANDOVER	SCOPE VALIDATION

#	JIRA	WORK PACKAGE	STATUS	CONTRIBUTORS
—	SA-15	Straight Bet	Post-Delivery	SBK, WBS
6	SA-66	Central Offer Foundation	In Delivery	SBK
2	SA-14	Soccer World Cup Hub	In Delivery	DATA, SBK, WBS
1	SA-17	Simple Parlay	In Delivery	SBK, WBS, WLT
3	SA-22	Settlement from Optic Odds	In Delivery	SBK, WLT
5	SA-20	Bet Placement Controls	In Delivery	SBK, WBS
7	SA-25	Bet Ticker	In Delivery	DATA, SBK
8	SA-24	RT Liability Reporting	In Delivery	DATA, SBK
13	SA-26	Bet History	In Delivery	BO, DATA, SBK
12	SA-27	My Bets	In Delivery	SBK, WBS

16	SA-71	Feed Provider Health	In Delivery	SBK
11	SA-19	RT Odds & Market Display	Ready for Handover	SBK, WBS
4	SA-21	Book & Player On/Off Switch	Ready for Handover	BO, DATA, PAM, SBK, WBS
9	SA-23	Manual Resettlement & Void	Ready for Handover	BO, DATA, SBK
10	SA-28	Audit Trail	In Delivery	SBK
14	SA-16	SGP	Scope Validation	SBK, WBS
15	SA-18	Mega Parlay	Scope Validation	SBK, WBS

Deliverable 1: Central Offering Foundation

> *Demo: Punter opens the sportsbook, sees World Cup fixtures, browses markets, odds update in real-time.*

FEEDS World Cup data flows from OpticOdds into our system. No feed = no sportsbook. Health monitoring protects from stale data.
WP 2, 6, 11, 16

OFFER We own our offer — not a pass-through of OpticOdds. Central Offer gives us control, future provider flexibility, and market management.
WP 2, 6, 11, 16

FRONTEND WC Hub landing page, structured navigation, real-time odds movement indicators, suspended market states.
WP 2, 6, 11, 16

BETTING SGP prices refresh when odds change. Betting stops accepting bets when feed is down.
WP 11, 16

DATA Odds line history for traders in Splunk. Data pipeline feeds Diffusion for real-time frontend. Feed health monitoring.
WP 2, 6, 11, 16

SPLUNK **RAW REPORT:** Offer events, odds history, feed health dashboard — first line of defense for traders.
WP 2, 6, 16

Deliverable 2: Betslip Core & Placement Flow

> *Demo: v1.55 — Punter places a straight bet with full validation. v1.6 — adds parlay, SGP, Mega Parlay. Operator controls limits and kill switch.*

FRONTEND Punter sees combined odds, potential winnings, clear errors. Kill switch makes site go dark instantly. SGP eligibility feedback.

WP 1, 4, 5, 14, 15

BETTING Core upgrade from prototype — parlay + SGP + Mega Parlay. Limit enforcement. Kill switch. Real wallet + auth integration.

WP 1, 4, 5, 7, 8, 13, 14, 15, 16

OFFER Business defines the rules — limits, allowed bet types, SGP/Mega Parlay configurations, master switch.

WP 4, 5, 14, 15

DATA Every bet attempt flows into reporting. Bet Ticker and Liability dashboards start working. Rejected bets analysis.

WP 1, 4, 5, 7, 8, 13, 14, 15, 16

SPLUNK **RAW REPORT:** First multi-leg bet events in the system. Feed health operational monitoring.

WP 1, 16

Deliverable 3: My Bets & Real Data Connection

> *Demo: Punter sees bet history updating live. Bets settle from real results. Traders correct errors. Real money moves.*

FRONTEND Punter sees "Pending to Won/Lost" on their bets. My Bets screen — core punter experience for transparency and trust.

WP 3, 12

BETTING Where the business makes or loses money. Real grading, real wallet credits/debits, resettlement, manual corrections, bet history.

WP 3, 7, 8, 9, 12, 13, 14, 15

FEEDS Match results flow from OpticOdds — without results, no bets settle.

WP 3

OFFER Results flow through our offer resolution — we own the grading, not the feed provider.

WP 3

DATA Settlement data feeds P&L reports. Liability updates as results arrive. Manual settlement audit. Live push for My Bets.

WP 3, 7, 8, 9, 12, 13

SPLUNK **RAW REPORT:** Every grading decision, every wallet transaction, every resettlement — the financial audit trail.

WP 3, 12

Deliverable 4: Operation Control & Visibility

> *Demo: Operator manages the book from Kraken. Splunk dashboards: feed health, bet ticker, liability, audit trail, bet history.*

BACKOFFICE Kraken tools — kill switch, limit config, manual settlement with justification, full audit trail. The operator's control panel.

WP 4, 5, 9, 10

BETTING Kill switch blocks the API (not just UI). Limits enforced at placement. Manual settlement engine. Audit for every action.

WP 4, 5, 7, 9, 10, 13

OFFER Operator Management holds the master switch and limit configuration — the source of truth for what's allowed.

WP 4, 5

DATA All operational dashboards — Bet Ticker, Liability, Audit Trail, Odds History, Feed Health, Rejected Bets analysis.

WP 4, 5, 7, 8, 9, 10, 11, 13, 16

SPLUNK **BUSINESS REPORT:** The trader's operational cockpit — every dashboard they need to run the book on game day.

WP 4, 5, 7, 8, 9, 10, 11, 13, 14, 15, 16

Domain Team Workload

WP assignments per team across all 4 deliverables. Betting and Data carry the heaviest load.

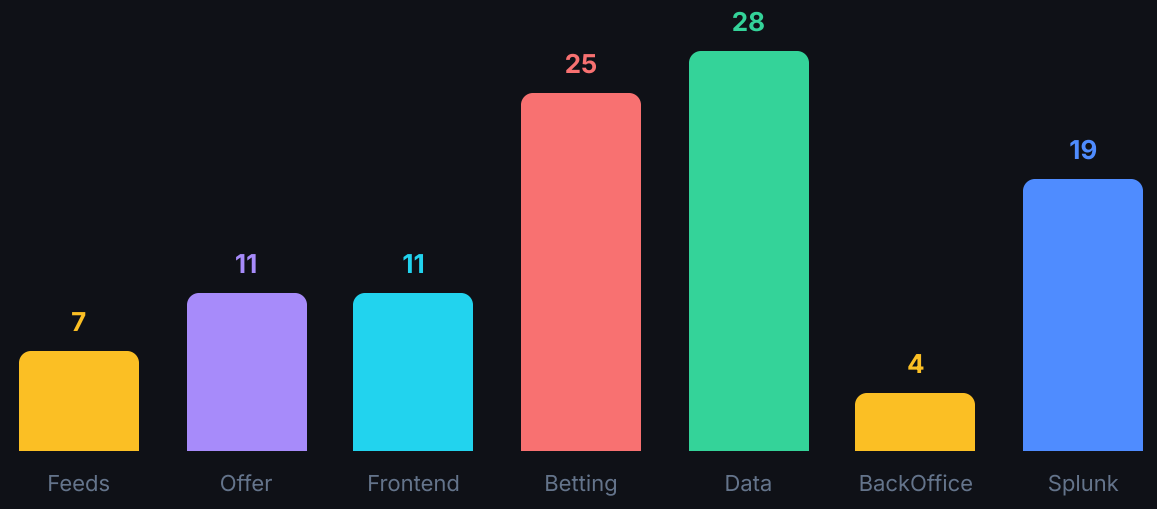

DOMAIN	D1	D2	D3	D4	TOTAL
Feeds	4	1	1	1	**7**
Offer	4	4	1	2	**11**
Frontend	4	5	2	—	**11**
Betting	2	9	8	6	**25**
Data	4	9	6	9	**28**
BackOffice	—	—	—	4	**4**
Splunk	3	2	2	12	**19**

Dependencies & Risks

CRITICAL PATH

WP 6 Central Offer → WP 2, 11, and all downstream Foundation

WES Wallet → WP 1, 3, 5, 9 Blocks 4 WPs

PAM Auth → WP 1, 5 Blocks 2 WPs

WP 1 Simple Parlay → WP 14 SGP → WP 15 Mega Sequential

TOP RISKS

HIGH **Mega Parlay & SGP still in Scope Validation**
Most complex bet types. Cannot estimate or plan until scope is locked.

HIGH **Shared DB schema refactor (SBK-2008)**
Tech debt blocking both Simple Parlay and Settlement.

HIGH **WES Wallet integration timeline**
Any delay cascades across 4 work packages. Real money can't move without it.

MED **Splunk vs New Relic strategy undefined**
Affects all reporting and audit WPs. Decision needed.

MED **Feed Health → Betting suspension unscoped**
When feed is unhealthy, who suspends betting? No WP owns this end-to-end.

Scope: v1.55 → v1.6 → Future

V1.55 — STRAIGHT BETS NOW

- ✓ **Straight Bets only** (single selection)
- ✓ Pre-match betting on World Cup fixtures
- ✓ Real settlement from OpticOdds results
- ✓ Operator controls (kill switch, limits, manual settle)
- ✓ Bet Ticker, Liability, Audit Trail in Splunk
- ✓ Web desktop + mobile responsive
- ✓ 4 brands, USD, en-US
- ✓ 5,000 bets/min | 500ms latency | 99.9% uptime

Reduced for v1.55

- ! Traders Hub UI — API only
- ! Limits config — absorbed into Betting

V1.6 — FULL BET TYPES NEXT

Everything in v1.55, plus:

- + **Simple Parlay** (multi-fixture, 2-12 legs)
- + **SGP** (same-game parlay, correlated pricing)
- + **Mega Parlay** (SGPs + straights combined)
- + Settlement for all bet types
- + Advanced limit validations per bet type

Should Have (v1.6)

- ~ In-Play betting
- ~ Futures betting (straights only)
- ~ Fractional odds format

V1.7+ / V2.0+ LATER

- ✗ Multi-currency
- ✗ Multi-language
- ✗ Cash Out
- ✗ Native mobile apps
- ✗ Custom markets
- ✗ Dynamic margin management
- ✗ Per-punter value factors
- ✗ Automated dispute dashboard
- ✗ Other sports

Planning Framework — 4 Zoom Levels

Each zoom level increases planning precision. Each level has a gate — work at that level only starts after the gate is passed.

01 Business Value Mapping

DONE

Gate: **Product + WPs defined**

What to Demo — Map each deliverable to demoable business value

What work per Domain — Assign WPs to domain teams with business WHY

Output: 4 Deliverables, 16 WPs mapped across 8 domains, business justification per assignment

02 Order & Estimates

NEXT

Gate: **After Architecture Handover**

What order per Domain — Sequence WPs within each domain based on dependencies and value

Super High Level Estimate — T-shirt sizing at weeks level (S/M/L/XL) per WP per domain

Dependencies — Cross-domain and external dependency map (WES, PAM, OpticOdds)

Output: Delivery order filled in sheet, T-shirt estimates, dependency graph per deliverable

03 Milestones & Dates

PENDING

Gate: **After Software Design**

Milestones / Demo Dates — Concrete dates for each deliverable demo

Estimation Per Big Feature — Man-day estimates based on software design output

Output: Programme timeline with demo milestones, resource allocation per feature

04 Sprint-Level Plan

PENDING

Gate: **After Team Refinement**

Story Points in a Sprint per Tasks — Detailed JIRA plan with story-level breakdown

Sprint assignments — Who does what in which sprint, velocity-based forecasting

Output: Full JIRA board with sprints, stories, assignments, burndown targets

SDLC Funnel — How Work Packages Progress

Each WP passes through a funnel of stages. Software Design is the unlock point — after that, work scales into teams for estimates and sprint planning.

Product
Scope & WP Definition
Owner: **Kurt / Stakeholders**
DOR

▶

Architecture
Coverage & Handover
Owner: **Matus / Solutions**
DOR DOD

▶

Software Design
UNLOCK POINT
Owner: **Team Principal**
DOR DOD

▶

Team Refine
Estimates & Planning
Owner: **Team Refine**
DOR DOD

▶

Team Execution
AWS Stage ▶ PPD ▶ Production
Owner: **Team Execution**
DOD

AFTER SOFTWARE DESIGN — WORK FANS OUT INTO PARALLEL STREAMS

Dev Estimates
Sprint → Demo

QA Estimates
Sprint → Demo

DevOps Plan
Sprint → Demo

Data Plan
Sprint → Demo

FE Plan
Before SD (Mocks)

Sprint Review 1
Iteration 1 Complete

▶

Sprint Review 2
Iteration 2 Complete

▶

Deliverable Demo
Business Value Shown

WP Progress Through the Funnel

Weekly tracking view — where each Work Package sits in the SDLC pipeline. Software Design completion is the key unblocking event.

#	WORK PACKAGE	PRODUCT	ARCHITECTURE	SOFTWARE DESIGN	TEAM REFINE	AWS STAGE	PPD	PRODUCTION	ETA / ITERATION
—	Straight Bet	✓	✓	✓	✓	✓	✓	✓	Delivered
6	Central Offer Foundation	✓	✓	In Progress	—	—	—	—	TBD
2	Soccer World Cup Hub	✓	✓	In Progress	—	—	—	—	TBD
1	Simple Parlay	✓	✓	In Progress	—	—	Iteration 1		
3	Settlement from Optic Odds	✓	✓	In Progress	—	—	—	—	TBD
5	Bet Placement Controls	✓	✓	In Progress	—	—	—	—	TBD
7,8	Bet Ticker + RT Liability	✓	✓	In Progress	—	—	—	—	TBD
12,13	My Bets + Bet History	✓	✓	In Progress	—	—	—	—	TBD
16	Feed Provider Health	✓	✓	In Progress	—	—	—	—	TBD
11	RT Odds & Market Display	✓	Ready	—	—	—	—	—	TBD
4	Book & Player On/Off Switch	✓	Ready	—	—	—	—	—	TBD

9	Manual Resettlement & Void	✓	Ready	—	—	—	—	—	TBD
10	Audit Trail	✓	Ready	—	—	—	—	—	TBD
14	SGP	Scope	—	—	—	—	—	—	Blocked
15	Mega Parlay	Scope	—	—	—	—	—	—	Blocked

Key insight: 9 WPs are currently in Software Design. Once each completes SD, it unlocks parallel estimation across Dev, QA, DevOps, Data, and FE streams — each producing sprint plans and demo targets. The SD column is the bottleneck we track weekly.

Work Package x Team Matrix

SBK-669 • HIGH-LEVEL VIEW

Which teams have epics per WP, with Jira key and status. Dashes = no epic exists yet for that team.

#	WORK PACKAGE	ARCHITECTS	BETTING ENG	OFFER MGMT	FEEDS MGMT	FEEDS INTEG	DATA	FRONTEND	BE QAS	UNASSIGNED
—	Straight Bet	Done SA-15	—	—	—	—	—	Active SBK-1951	To Do SBK-3790	—
6	Central Offer	In Del SA-66	—	Scoping SBK-3006	—	—	—	—	—	—
2	Soccer WC Hub	In Del SA-14	—	—	Active SBK-1897 Scoping SBK-3516	—	—	—	—	To Do SBK-2189
1	Simple Parlay	In Del SA-17	Active SBK-2199	—	—	—	—	—	—	—
3	Settlement	In Del SA-22	—	—	—	—	—	—	—	To Do SBK-2200
4	Book On/Off	Ready SA-21	—	—	—	—	—	—	—	To Do SBK-2201
5	Bet Controls	In Del SA-20	—	—	—	—	—	—	—	To Do SBK-2202
7	Bet Ticker	In Del SA-25	—	—	—	—	Active DATA-22	—	—	To Do SBK-2217
8	RT Liability	In Del SA-24	—	—	—	—	—	—	—	To Do SBK-2216

9	Manual Resettlement	Ready SA-23	—	—	—	—	—	—	—	To Do SBK-2215
10	Audit Trail	In Del SA-28	—	—	—	—	—	—	—	To Do SBK-2220
11	RT Odds Display	Ready SA-19	—	—	—	—	—	—	—	To Do SBK-2214
12	My Bets	In Del SA-27	—	—	—	—	—	—	—	To Do SBK-2219
13	Bet History	In Del SA-26	—	—	—	—	—	—	—	To Do SBK-2218
14	SGP	Scope SA-16	—	—	—	—	—	—	—	—
15	Mega Parlay	Scope SA-18	—	—	—	—	—	—	—	—
16	Feed Health	In Del SA-71	—	—	—	Active SBK-3094	—	—	—	—

6
TEAM EPICS ACTIVE

11
PLACEHOLDER "DELIVERY"

~40+
MISSING TEAM EPICS

Action: Most WPs only have the SA-* architecture epic + a "Delivery" placeholder. Per the FINAL-PLAN, each WP needs team-specific epics for every contributing domain.

Epic Progress Per Work Package

SBK-669 • LIVE FROM JIRA

Each team epic with child ticket breakdown: To Do / In Progress / Done. Progress bar shows % complete.

EPIC	TEAM	TICKETS	PROGRESS	DONE %	STATUS
[FE] Straight Bet SBK-1951	Frontend	39	23 Done · 15 In Prog · 1 To Do	59%	In Progress
[BE] Simple Parlay SBK-2199	Betting Engine	34	29 Done · 5 In Prog · 0 To Do	85%	In Progress
[BE] Central Offer Foundation SBK-3006	Offer Mgmt	17	10 Done · 7 In Prog · 0 To Do	59%	Scoping
[WC] Market Parser Digestion SBK-1897	Feeds Mgmt	11	10 Done · 1 In Prog · 0 To Do	91%	In Progress
[BE] Feed Provider Health SBK-3094	Feeds Integ	10	4 Done · 3 In Prog · 3 To Do	40%	In Progress
[BE] Settlement from Optic Odds SBK-2200	Delivery	9	6 Done · 3 In Prog · 0 To Do	67%	To Do
Soccer World Cup Hub SBK-2189	Delivery	9	9 To Do	0%	To Do
FUTURO - Bet Ticker/History DATA-22	Data	9	5 In Prog · 4 To Do	0%	In Progress
Resulting for Pre Game Markets SBK-3516	Feeds Mgmt	1	1 To Do	0%	Scoping
[QA] Straight Bet E2E Validation SBK-3790	BE QAs	1	1 In Prog	0%	To Do

82	39	18	139	59% Overall Complete
DONE	IN PROGRESS	TO DO	TOTAL TICKETS	

Epic Timeline — March to August 2026

START & DUE DATES FROM JIRA

Delivery epics only (not architecture SA-∗ epics). Bars show start→due date range. Grey = no due date set.

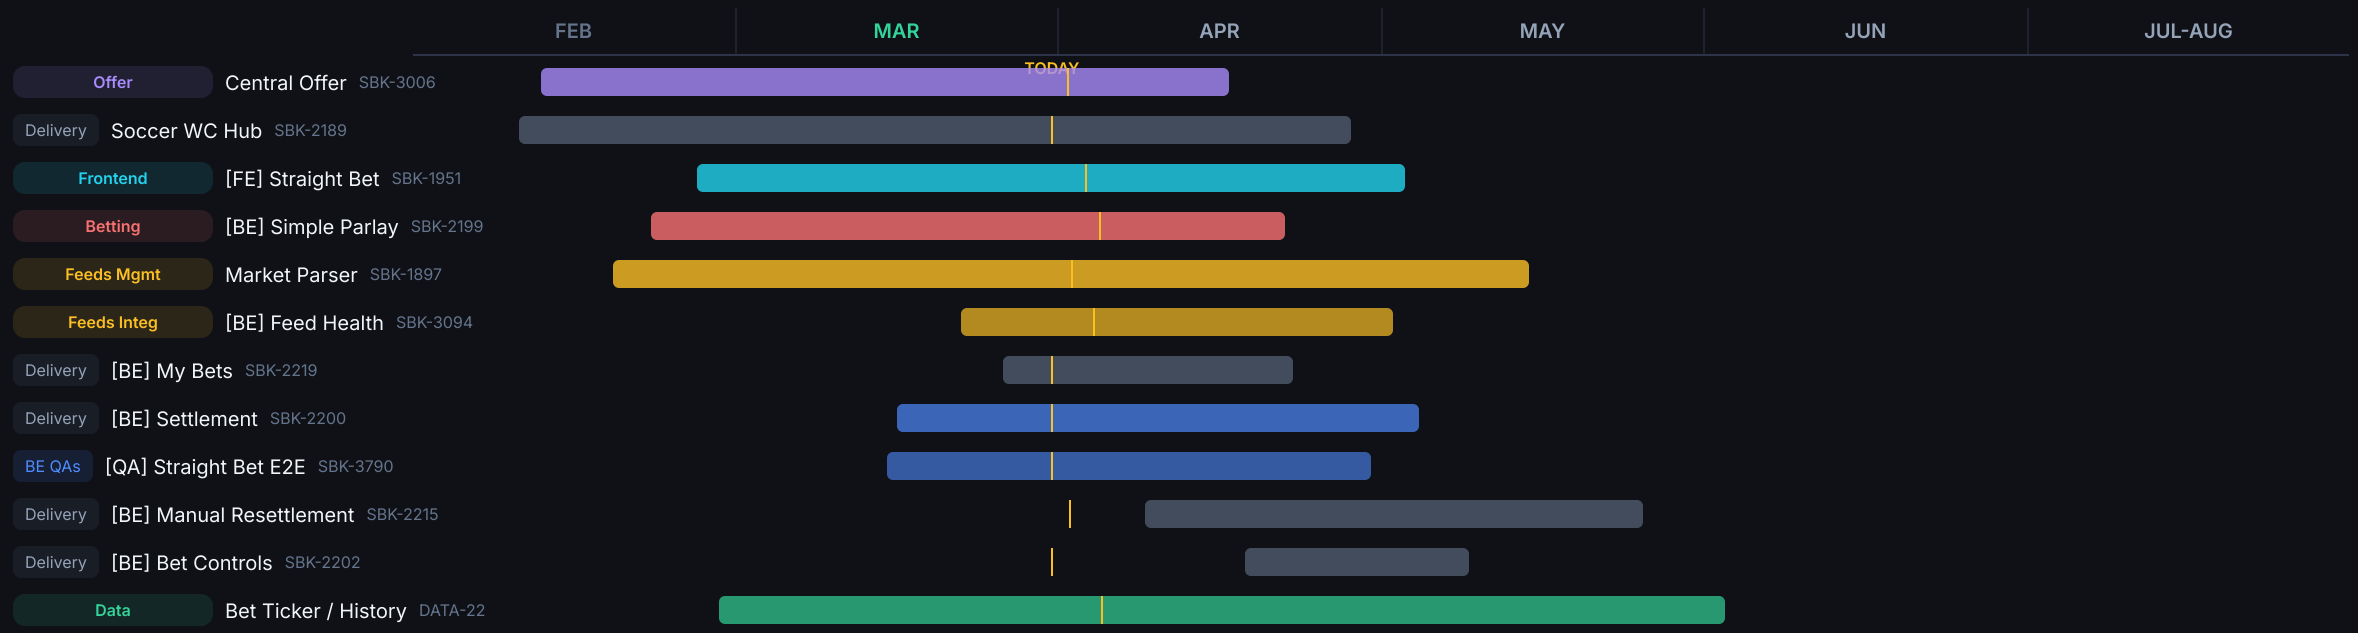

Apr 1
SOFT LAUNCH

May 1
GO-LIVE

Mid-June
WORLD CUP

6 delivery epics have no due date — these need dates set to enable timeline planning. Feeds Market Parser (May 15) and Data Bet Ticker (Jun 1) are the longest-running epics.

Epic Dependency Map

FROM JIRA "BLOCKS" LINKS

Three independent dependency chains. An epic cannot start until its blocker is complete.

CHAIN 1: OFFER & HUB FOUNDATION

SA-66 Central Offer Foundation
Offer Management • Due: Apr 15
In Delivery

▼

SA-14 Soccer World Cup Hub
Feeds + Offering • Due: Apr 29
In Delivery

▼

SA-19	SA-20	SA-21
RT Odds Display	Bet Controls	Book On/Off
Ready	In Del	Ready

CHAIN 2: BET TYPES (V1.55 → V1.6)

SA-15 Straight Bet
COMPLETED • Post-Delivery Assessment
Done

▼

SA-17 Simple Parlay
Betting Engine • Due: Apr 20
In Delivery

▼

SA-16 SGP
BLOCKED — Scope Validation
Scope

▼

SA-18 Mega Parlay
BLOCKED — Scope Validation
Scope

CHAIN 3: SETTLEMENT + INDEPENDENT

SA-22 Settlement from Optic Odds
Betting + Wallet • Due: May 6
In Delivery

▼

SA-23 Manual Resettlement & Void
Betting + BackOffice • Due: May 25
Ready

NO DEPENDENCIES (CAN START ANYTIME)

SA-24	SA-25	SA-26	SA-27	SA-28
RT Liability	Bet Ticker	Bet History	My Bets	Audit Trail

SA-71
Feed Health

Critical path: SA-15 → SA-17 → SA-16 → SA-18 is the longest sequential chain (Straights → Parlay → SGP → Mega). SGP and Mega are blocked until Simple Parlay completes.

Foundation chain: SA-66 → SA-14 gates three downstream WPs (RT Odds, Bet Controls, Book On/Off). Central Offer must land first.

Parallelizable: 6 WPs have no blockers — RT Liability, Bet Ticker, Bet History, My Bets, Audit Trail, Feed Health. These can progress independently.

Where We Are & Next Steps

CURRENT POSITION IN THE PIPELINE



WP PIPELINE STATUS

GATE REQUIREMENTS FOR ZOOM LEVEL 02

WP STATUS	COUNT	CAN START Z02?
In Delivery	11	Yes — architecture handed over
Ready for Handover	4	Yes — once delivery picks up
Scope Validation	2	No — SGP + Mega Parlay blocked

IMMEDIATE ACTIONS

Unblock SGP & Mega Parlay

Architecture team to complete scope validation for SA-16 and SA-18 — currently blocking Zoom Level 02 for these WPs

Start Zoom Level 02 for 15 WPs

DMs to fill in delivery order, T-shirt estimates (weeks), and cross-domain dependencies for the 15 WPs past architecture gate

Platform Decision: Splunk vs New Relic

Affects 8+ reporting/audit WPs across Deliverables 2-4. Decision needed before Z02 estimates for Data team

Confirm External Timelines

WES Wallet (blocks 4 WPs) and PAM Auth (blocks 2 WPs) — integration timelines needed for Z02 dependency mapping

Pick Up 4 Handover WPs

RT Odds Display, Book On/Off Switch, Manual Resettlement, Audit Trail — architecture complete, waiting for delivery capacity

APPENDIX A

Business WHY Matrix — Deliverables 1 & 2

For each domain × WP: what business need does it serve? What do we demo?

DELIVERABLE 1: CENTRAL OFFERING FOUNDATION

DOMAIN	WP	BUSINESS WHY
FEEDS	2	WC data must flow from OpticOdds — no feed, no sportsbook
FEEDS	6	Richer data needed — more markets, metadata, statistics for competitive product
FEEDS	11	Odds must reach punter fast enough to bet confidently — stale odds = lost trust
FEEDS	16	Detect unhealthy OpticOdds, protect punters from stale data
OFFER	2	We own our offer — not a pass-through. We control what punters see
OFFER	6	Foundation for independent offer management — future provider flexibility
OFFER	11	Odds flow through our pipeline — we control the last mile to punter
FRONTEND	2	WC Hub landing page — discover matches, view groups, start betting
FRONTEND	6	Structured navigable offering — not raw feed data
FRONTEND	11	Real-time odds movement + suspended market indicators — builds trust
BETTING	11	SGP prices refresh when odds change — accurate combined price always
DATA	2	Traders need odds line history in Splunk
DATA	6	Data pipeline needs unified offer model for reports
DATA	11	Data feeds Diffusion for real-time frontend updates

DELIVERABLE 2: BETSLIP CORE & PLACEMENT

DOMAIN	WP	BUSINESS WHY
FRONTEND	1	Combine selections from different matches, see combined odds + winnings
FRONTEND	4	Kill switch makes site go dark instantly — clear "unavailable" state
FRONTEND	5	Max stake visible, clear errors on limit breach — no guessing
BETTING	1	Core upgrade from prototype — parlay bets, not just straights
BETTING	4	If operator says stop, no bets get through — risk management essential
BETTING	5	Every bet validated against limits — protects from unbounded risk
BETTING	7	Every bet placed/rejected appears in trader's live feed
BETTING	8	As bets come in, exposure grows — traders see this in real-time
OFFER	4	Master switch + per-offering controls to disable bet types
OFFER	5	Business defines limits — min/max stake, max payout, max legs
DATA	1	New bet type = new data in reports — parlays in ticker + liability
DATA	7	Core data product — live scrolling bet feed with full context
DATA	8	Core data product — real-time exposure by market + fixture

APPENDIX B

Business WHY Matrix — Deliverables 3 & 4

DELIVERABLE 3: MY BETS & REAL DATA

DOMAIN	WP	BUSINESS WHY
FRONTEND	3	Punter sees "Pending → Won/Lost" — the moment of truth
FRONTEND	12	My Bets anytime — active + settled bets. Core punter experience
BETTING	3	Where business makes/loses money — real grading, real wallet credits/debits
BETTING	9	Traders override incorrect results — void bad markets, correct grading
BETTING	12	Bet history updates live — "just settled" without page refresh
BETTING	13	Traders investigate any bet's full lifecycle — placement through settlement
FEEDS	3	Results from OpticOdds — without results, no bets settle
OFFER	3	Results through our resolution — we own the grading
DATA	3	Settlement feeds P&L reports — business knows if it's winning
DATA	9	Manual settlement audit — payout volumes, goodwill costs
DATA	12	Real-time push for My Bets — "your bet just won"

DELIVERABLE 4: OPERATION CONTROL & VISIBILITY

DOMAIN	WP	BUSINESS WHY
BACKOFFICE	4	Kill switch in Kraken — shut down sportsbook in emergency
BACKOFFICE	5	Configure stake/payout limits — control book's risk appetite
BACKOFFICE	9	Manual settle UI — search bets, apply corrections, add justification
BACKOFFICE	10	Every trader action logged — who changed what, when, why
BETTING	4	Kill switch blocks API not just UI — belt and braces
BETTING	5	Limits enforced at placement — last line before money moves
BETTING	9	Settlement engine accepts manual corrections + wallet reversals
BETTING	10	Every betting action produces audit record — full traceability
DATA	7	Bet Ticker dashboard — traders' primary live monitoring tool
DATA	8	Liability dashboard — primary risk management tool
DATA	10	All actions searchable in one place — compliance + investigation
DATA	11	Odds line history + latency monitoring — are we meeting SLAs?
SPLUNK	4-16	Trader's operational cockpit — every dashboard for game day

APPENDIX C

Technical WHY — Requirement IDs per Domain × WP

Each assignment backed by specific requirement IDs from the V1.6 Requirements Document.

DELIVERABLE 1 & 2 — KEY REQUIREMENTS

DOMAIN × WP	REQUIREMENT IDS
FRONTEND × WP 2	UC-02, FE-004, FE-001, FE-002
FRONTEND × WP 6	UC-02, MKT-005, INT-006
FRONTEND × WP 11	MKT-005, MKT-006, MKT-012, MKT-001/002, MKT-004
FEEDS × WP 2	INT-003, NFR-002, MKT-005
FEEDS × WP 6	NFR-002 (Feed Throughput)
OFFER × WP 2	UC-02, MKT-012, RPT-006
OFFER × WP 6	UC-02, all offer-related reqs
BETTING × WP 11	INT-002, BET-009
BETTING × WP 1	UC-08, BET-003, BET-005, INT-004, INT-005, BET-013
BETTING × WP 4	OPR-003, UC-29, UC-34, OPR-008
BETTING × WP 5	LIM-001 to LIM-006, BET-008, BET-009, NFR-006
OFFER × WP 4	OPR-003, OPR-004, OPR-005
OFFER × WP 5	OPR-007, LIM-001 to LIM-010, UC-33
DATA × WP 7	RPT-001/002/003, UC-28

DELIVERABLE 3 & 4 — KEY REQUIREMENTS

DOMAIN × WP	REQUIREMENT IDS
BETTING × WP 3	SET-001, SET-004, SET-006, BET-005, INT-004, NFR-004
BETTING × WP 9	SET-002, SET-003, SET-005, UC-23
BETTING × WP 12	UC-11, UC-12, FE-003
FRONTEND × WP 3	FE-003, BET-011
FRONTEND × WP 12	UC-11, UC-12, FE-003
DATA × WP 3	RPT-008, RPT-004
DATA × WP 9	SET-005, RPT-008
DATA × WP 12	FE-003, INT-006
BACKOFFICE × WP 4	OPR-003, OPR-009, UC-29, UC-34
BACKOFFICE × WP 5	UC-33, OPR-007
BACKOFFICE × WP 9	SET-002, SET-003, SET-005, UC-23
BACKOFFICE × WP 10	UC-32, NFR-007
DATA × WP 10	UC-32, NFR-007
DATA × WP 11	MKT-005, NFR-001

DATA × WP 8	RPT-004, RPT-005, UC-27
SPLUNK × WP 4-16	RPT-001 to RPT-010, UC-25 to UC-32

Source: Futuro Sportsbook Platform V1.6 Requirements for FIFA World Cup 2026 — 150+ requirements across 14 categories (BET, MKT, LIM, SET, RPT, FE, NFR, OPR, INT, BSL, PCF, PEND, SCO)

APPENDIX D

Work Package Architecture Summary

Key facts per WP from Confluence architecture coverage. Full report: reports/work-package-report.md

#	WP	NEW COMPONENTS	KEY DEPENDENCIES
6	Central Offer	Offer Processor + DB, Resolution + DB, Config + DB, Redis Cache, Schema Registry	Feeds ID generation, Pulsar topics
2	WC Hub	Unifier feature flags, Offer Health Monitor	SA-66 foundation, Batch 1 markets
1	Simple Parlay	PAM Adapter (JWT), Wallet Adapter (WES), Clear Betslip endpoint	SBK-2008 DB refactor, SBK-2056 API decoupling
3	Settlement	RolledBackLegsProcessor, WalletResultsProcessor, Offer Resolution consumer	WES wallet, SA-66 offer resolution
4	Book On/Off	Betting Risk Control Service (CQRS), Punter Risk Cache (Redis)	Pulsar events from Operator/Punter Mgmt
5	Bet Controls	Validation engine in BetPlacement	PAM + WES from SA-17
7	Bet Ticker	Business Event Enricher (Data Platform)	Pulsar bet events from Betting
8	RT Liability	Business Event Enricher (shared with WP7)	Pulsar bet events from Betting

#	WP	NEW COMPONENTS	KEY DEPENDENCIES
9	Manual Resettle	Bet Settlement API (NEW), Bet Management UI in Kraken	SA-22 settlement engine
10	Audit Trail	Structured logging + Cloud Events + OTEL across ALL services	Cross-cutting — all domains
11	RT Odds Display	Diffusion integration, UX polish	SA-14, SA-27, SA-21
12	My Bets	Bet Query Service (CQRS), Bet Read Model Cluster, Bet Query API	Bet Settlement prerequisite
13	Bet History	Shares Bet Query Service with WP12, Traders Hub UI (API only for MVP)	SA-27 backend
14	SGP	OpticOdds Co-Pilot integration, SGP pricing API	SA-17 parlay foundation
15	Mega Parlay	Complex combination engine, repeated Co-Pilot calls	SA-16 SGP, performance risk
16	Feed Health	Health Watchdog (NEW), Feed Recovery Service (NEW)	Offer/Betting suspension NOT scoped

APPENDIX E

Key References & Performance Targets

DOMAIN TEAM LEADS

DOMAIN	LEAD
FE / Frontend	Kurt / Fede
FEEDS (Architecture)	Matus / Arch Lead
FEEDS (Integration)	Edu Ortega
OFFER (Product)	Vassilis Iliopoulos
OFFER (Delivery)	Juan / Ceci
BETTING (Product)	Juan Ballesta
BETTING (Delivery)	Dev Manager BE / Jul
DATA	Jose Marmolejo / Kurt
SITE	e.moreno

PERFORMANCE TARGETS (NFR)

METRIC	TARGET
Odds latency (provider → screen)	500ms max
Feed throughput	1,000 msgs/sec
Bet placement throughput	5,000 bets/min

CONFLUENCE & JIRA REFERENCES

RESOURCE	REFERENCE
WP List (Architecture)	Confluence page 1312129102
V1.6 Requirements	Confluence page 1145077761
Official Pages	Confluence page 1396047969
Jira Initiative	SBK-669
WP Filter (Architecture)	Jira filter 14152
WP Filter (Delivery)	Jira filter 14555

CONTRIBUTOR LABELS (JIRA)

LABEL	TEAM
wch_cntrbtr_SBK	Sportsbook (Feed, Offer, Betting)
wch_cntrbtr_WBS	WebSites
wch_cntrbtr_DATA	Data Platform (Splunk reports)
wch_cntrbtr_PAM	PAM (Auth)
wch_cntrbtr_WLT	Wallet (WES)
wch_cntrbtr_BO	BackOffice (Kraken 2)

Settlement processing	200 seconds from result
Uptime	99.9% (43 min/month max)
Load test target	150% peak: 75K users, 7.5K bets/min

GENERATED REPORTS (IN THIS REPO)

FILE	CONTENT
work-package-report.md	Deep-dive per WP from Confluence
why-matrix-business.md	Business WHY per domain × WP
why-matrix.md	Technical WHY with requirement IDs

Timeline: Phase 1 — Offering Foundation

LABEL: PHASE1-OFFERINGFOUNDATION

Focus: Updated view including all newly assigned epics.

COMMITTED DELIVERY DATE

May 15, 2026

STATUS

Active Delivery

	FEB	MAR	APR	MAY-JUN
[BE] Central Offer Foundation (SBK-3006)				
Soccer WC Hub (SBK-2189)				
Market Parser (SBK-1897)				
[QA] Straight Bet Validation (SBK-3790)				
Feed Health Monitoring (SBK-3094)				
Resulting for Pre Game Markets (SBK-3516)				

Phase 1 covers the core ingestion and Hub structure. Market Parser remains the gating item.

Focus: Establishing the core data digestion, central offering models, and market parsing capabilities.

COMMITTED DELIVERY DATE

May 15, 2026

STATUS

Active Delivery

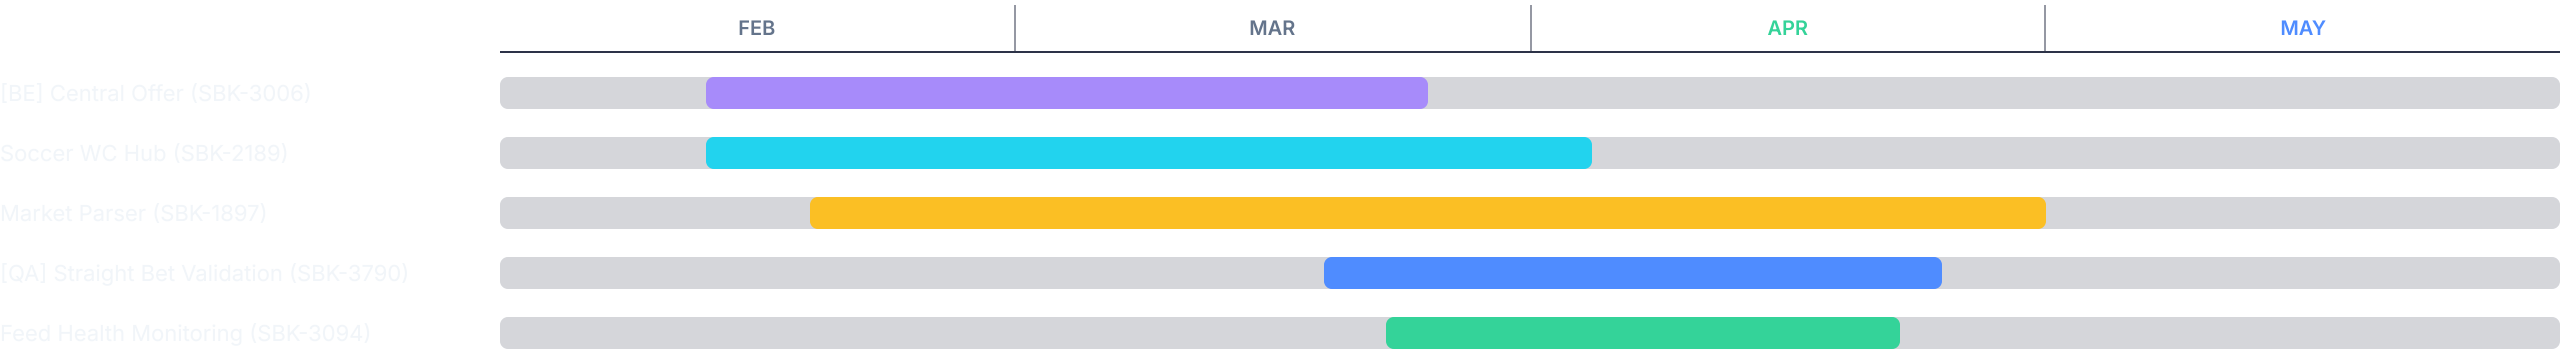

Critical Dependency: The delivery of the Market Parser (May 15) is the gating item for Phase 1 completion. All other foundation epics are scheduled to complete by early May.

Timeline: Phase 2 — Betslip Core & Placement Flow

LABEL: PHASE2-BETSLIPCORE&PLACEMENTFLOW

Focus: Updated view including all newly assigned epics.

COMMITTED DELIVERY DATE

June 01, 2026

STATUS

Active Delivery

	FEB	MAR	APR	MAY-JUN
[BE] Simple Parlay (SBK-2199)				
[BE] Settlement from OO (SBK-2200)				
[BE] Bet Placement Controls (SBK-2202)				
[BE] Manual Resettle & Void (SBK-2215)				
Bet History (SBK-2218)				
Bet Ticker (SBK-2217)				
Real-Time Liability Reporting (SBK-2216)				
Book & Player On/Off Switch (SBK-2201)				
Real-Time Odds & Market Display (SBK-2214)				

Phase 2 scope expanded with additional monitoring and display epics. Completion date moved to June 1st to accommodate Manual Resettlement tools.

Focus: Core betting logic, parlay support, and placement validations.

COMMITTED DELIVERY DATE

May 25, 2026

STATUS

Active Delivery

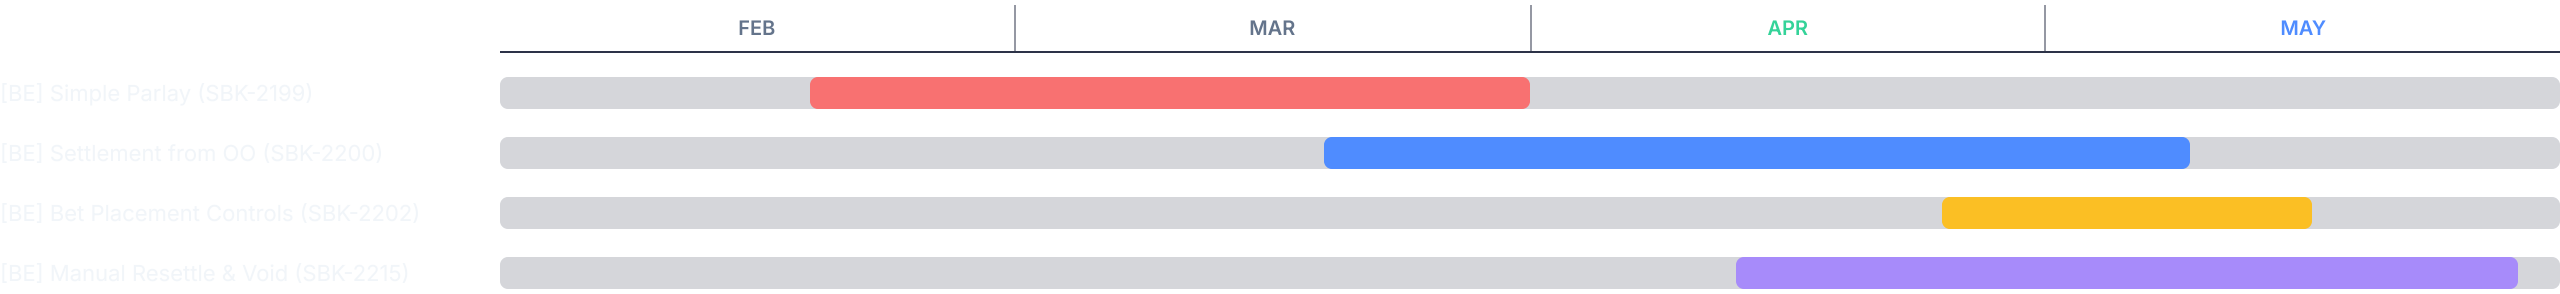

Phase 2 Completion: May 25 marked by the delivery of manual resettlement tools. Core placement and automated settlement complete by mid-May.

Timeline: Phase 3 — Post-Bet Transparency

LABEL: PHASE3-POSTBETTRANSPARENCY

Focus: Updated view including all newly assigned epics.

COMMITTED DELIVERY DATE

June 01, 2026

STATUS

Active Delivery

	FEB	MAR	APR	MAY-JUN
[BE] My Bets (SBK-2219)				
Bet History (SBK-2218)				
Bet Ticker (SBK-2217)				
Real-Time Liability Reporting (SBK-2216)				
[BE] Settlement from OO (SBK-2200)				
[BE] Manual Resettle & Void (SBK-2215)				

Phase 3 focuses on the punter's post-bet experience. Shared lifecycle with Phase 2 settlement epics.

Focus: Punter experience after placement — history, status updates, and settlement visibility.

COMMITTED DELIVERY DATE

May 25, 2026

STATUS

In Progress



Synergy with Phase 2: Phase 3 overlaps significantly with Phase 2 as the betting backend handles both placement and post-placement lifecycle. Punter-facing history (My Bets) lands early in the cycle.

Timeline: Phase 4 — Operation Control & Visibility

LABEL: PHASE4-OPERATIONCONTROLANDVISIBILITY

Focus: Updated view including all newly assigned epics.

COMMITTED DELIVERY DATE

June 01, 2026

STATUS

Active Delivery



Bet Ticker / History (DATA-22)

[BE] Manual Resettlement & Void (SBK-2215)

Book & Player On/Off Switch (SBK-2201)

> Phase 4 provides the internal tools for traders. Delivery centered around the unified Data dataset.

Focus: Internal dashboards, risk monitoring, and operational controls for traders.

COMMITTED DELIVERY DATE

June 01, 2026

STATUS

Refining Dates



Long-term Delivery: Operational datasets and advanced reporting (DATA-22) extend into June. Basic control switches and manual management land in Phase 2/3.
